



Guam Transportation Program Project Updates

Carl V. Dominguez

Director

Jay Rojas

Deputy Director

June 5, 2013

Roadway Construction Highlights

- 23 projects worth \$90 million are complete.
- 3 projects worth \$30 million are under construction:
 - Route 4; Pago Bay to Route 17
 - Ylig Bridge Replacement
 - Route 1/8 Intersection and Agana Bridges Replacement
- Construction will begin on 3 projects (\$7 M) within 3 months:
 - Agfayan Bridge Replacement (Route 4)
 - Asan and Aguada Bridges (Route 1)
 - Jinapsan Beach Road

COMPLETED PROJECTS

MAY 30, 2013

1 Guatali Route 2A, Temporary Restoration of Guatali Bridge and Embankment

Contractor: Chi Construction
Completed: November 2008
Final Cost: \$187,704

2 Route 1 U-Turn Reconstruction (Tamuning)

Contractor: Maeda Pacific Corp.
Completed: February 2009
Final Cost: \$137,690

3 Tinaga Bridge Permanent Restoration

Contractor: BME & Sons, Inc.
Completed: August 2009
Final Cost: \$223,685

4 Route 15 (in front of DOC, Mangilao)

Contractor: Maeda Pacific Corp.
Completed: December 2009
Final Cost: \$649,279

5 Skatepark Barrier/Iglesia Circle Traffic Signal

Contractor: Kinden Corp.
Completed: March 2010
Final Cost: \$562,923

18 Route 11 Improvements and Traffic Enforcement Screening Station

Completion: May 2013
Contractor: Core Tech International
Final Cost: \$17.1M

19 Route 11 Shore Protection

Completion: April 2013
Contractor: Core Tech International
Final Cost: \$5.2M

20 Taleyfak Bridge Restoration

Completion: May 2013
Contractor: Rex International
Final Cost: \$9M

ISLANDWIDE

1i Islandwide Guardrail Replacement Phase 1

Contractor: Orion Construction Corp.
Completed: February 2010
Final Cost: \$4.54M

2i Islandwide LED Signal Light Upgrade

Contractor: Kinden Corporation
Completed: March 2010
Final Cost: \$521,875

3i GPS Lock and Loops

Contractor: Kinden Corporation
Completed: March 2010
Final Cost: \$91,255

4i Islandwide Pavement Markings Improvement Phase 1

Contractor: Nippo Construction
Completed: April 2010
Final Cost: \$2.09M

5i Islandwide Pavement Markings Improvement Phase 2

Contractor: Highway Safety Services
Completed: March 2010
Final Cost: \$1.63M

6i Islandwide Guardrail Replacement Phase 2

Contractor: Nippo Corporation
Completed: July 2010
Final Cost: \$3.22M

7i Islandwide and School Zone Signs

Contractor: Highway Safety Services
Completed: December 2011
Final Cost: \$300,000

11 Route 25 (Alageta Road)

Contractor: Guam Construction Company, Inc.
Completed: July 2012
Final Cost: \$7.4M

12 Route 16/GMF Post Office/Army National Guard Intersection Signal Upgrade

Contractor: Maeda Pacific Corp.
Completed: July 2012
Final Cost: \$1.5M

13 Route 8/10/16 Tri Intersection

Contractor: Kinden Corporation
Completed: June 2012
Final Cost: \$5.1M

14 Rehabilitation of Route 4 Bridges (Talofofo & Togcha River)

Contractor: Black Construction
Completed: August 2012
Final Cost: \$4.0M

15 Route 7A Resurfacing

Completed: December 2012
Contractor: Sumitomo Mitsui Const. Co.
Final Cost: \$5.5M

16 Route 4 Resurfacing & Widening (McDonalds to Route 10)

Completed: December 2012
Contractor: Hawaiian Rock Products
Final Cost: \$16.6M

17 Route 17 Rehabilitation and Widening

Completion: February 2013
Contractor: Sumitomo Mitsui
Final Cost: \$6M

6 Masso River Bridge Embankment

Contractor: Chi Construction
Completed: December 2011
Final Cost: \$330,000

7 Route 15 Embankment Restoration

Contractor: International Bridge Corp.
Completed: March 2012
Final Cost: \$650,000

8 Route 2 Culverts & Slide Repair


Contractor: IMCO
Completed: February 2012
Final Cost: \$3.8M

9 Route 6A Murray Road, Maina-Nimitz Hill

Contractor: Rex International
Completed: April 2012
Final Cost: \$360,000


10 North Guam Signalization

Contractor: Beijess Enterprises Inc., GEMCCO
Completed: August 2012
Final Cost: \$1.1 M

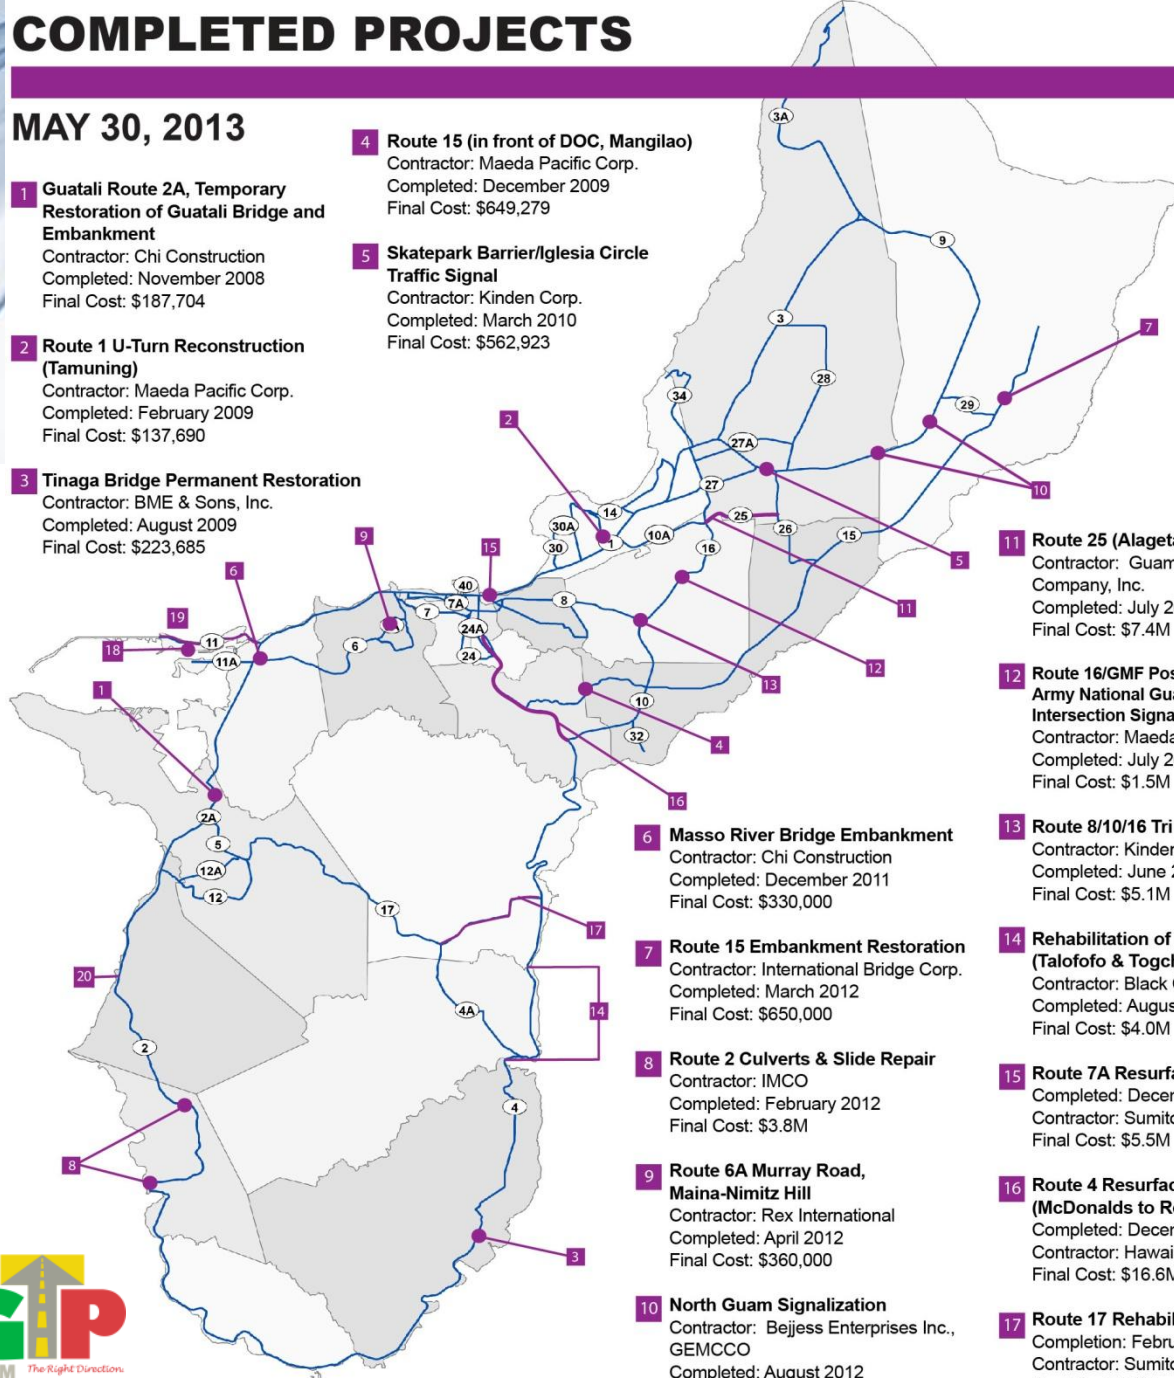

CURRENT CONSTRUCTION PROJECTS

MAY 30, 2013

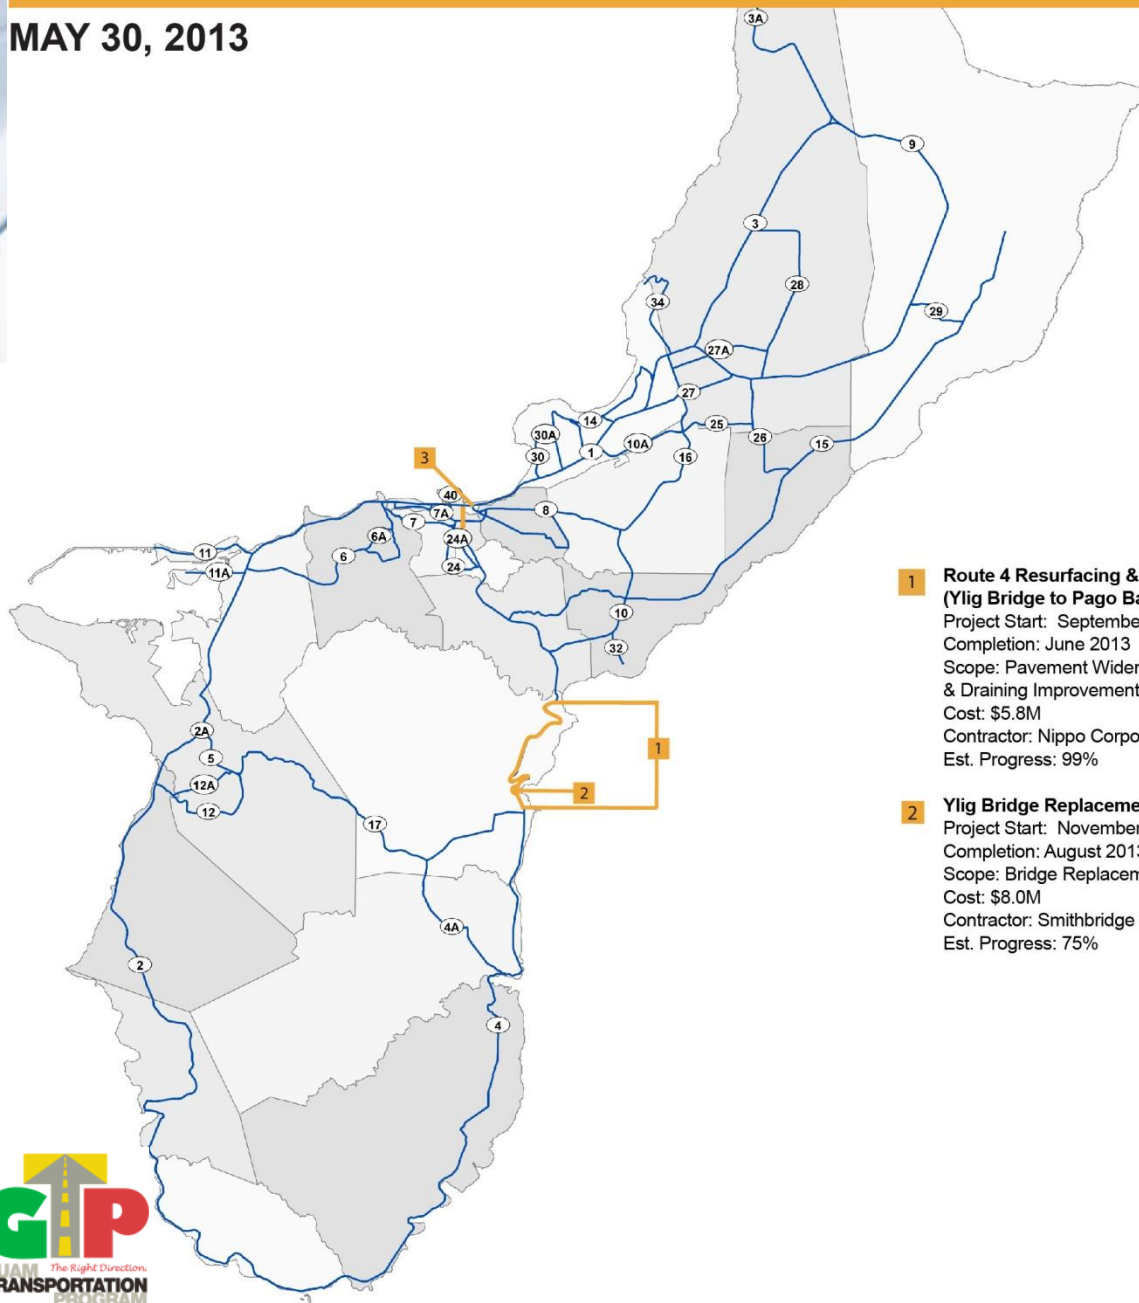

**1 Route 4 Resurfacing & Widening
(Ylig Bridge to Pago Bay)**

Project Start: September 2010
Completion: June 2013
Scope: Pavement Widening, Resurfacing
& Draining Improvements
Cost: \$5.8M
Contractor: Nippo Corporation
Est. Progress: 99%

2 Ylig Bridge Replacement

Project Start: November 2010
Completion: August 2013
Scope: Bridge Replacement
Cost: \$8.0M
Contractor: Smithbridge Guam, Inc.
Est. Progress: 75%

**3 Route 1/8 Intersection Improvements
and Agana Bridge Replacement
(Design Build)**

Project Start: September 2011
Completion: October 2014
Scope: Road improvements and Bridges
Replacement
Cost: \$16.4M
Contractor: Core Tech International
Est. Progress: 40%

Route 1/8 Intersection Agana Bridges Project

- Contractor: Core Tech International - \$16.4 million
- Current expected completion date (all work): October 2014
- Current expected completion date for Agana Bridge and Route 1 and Route 8 work: December 2013
- Project Issues:
 - Underground Utilities
 - Archeological

PLANNING & DESIGN

MAY 30, 2013

DESIGN PROJECTS

1 Inarajan North Leg (As-Misa) Bridge Scour Repair

Status: Design in Progress
Estimated Construction Cost: \$2.4M
Designer: NC Macario & Associates

2 Agfayan Bridge Replacement

Status: Construction Contract Pending
Estimated Construction Cost: \$4.7M
Designer: GHD

3 Ajayan Bridge Replacement

Status: Design in Progress
Estimated Construction Cost: \$3.5M
Designer: NC Macario & Associates

9 Route 27, Finegayan Road (Harmon Cutoff) Phase 1

Status: Design in Progress
Estimated Construction Cost: \$12.7M
Designer: Duenas Camacho & Associates

10 Traffic Signal Upgrade, Islandwide

Status: Design in Progress
Estimated Construction Cost: \$1.8M
Designer: EMCE Consulting Engineers

11 Route 17 Drainage Culverts

Status: Design in Progress
Estimated Construction Cost: \$1.7M
Designer: Duenas Camacho & Associates

12 Route 17 Rehabilitation

Status: Design in Progress
Estimated Construction Cost: \$9.0M
Designer: Duenas Camacho & Associates

13 Asan & Aguada Bridges Rehabilitation

Status: Construction Contract Pending
Estimated Construction Cost: \$1.1M
Designer: Duenas Camacho & Associates

14 Route 14B, Ypao Road

Status: Design in Progress
Estimated Construction Cost: \$10.8M
Designer: EM Chen & Associates

15 Route 29 Reconstruction

Status: Design in Progress
Estimated Construction Cost: \$5.2M
Designer: TG Engineers

16 Route 4 Curve Widening

Status: Pending Approval
Estimated Construction Cost: \$3.5M
Designer: AECOM

17 Tiyan Parkway, Phase 1

Status: Design in Progress
Estimated Construction Cost: \$9.9M
Designer: Duenas, Camacho & Associates

18 Rt 26/25 Intersection Improvements

Status: Design in Progress
Estimated Const. Cost: \$3.1M
Designer: Parsons Brinckerhoff

CURRENTLY ON HOLD

19 Traffic Management Center – Communications


Status: On Hold
Estimated Construction Cost: \$2.0M
Designer: Parsons Brinckerhoff

20 Rts 1/3 Intersection Improvements

Status: Survey completed.
Design on hold by the DOD.
Estimated Construction Cost: \$9.3M
Designer: TG Engineers

21 Route 3 Widening Route 28 - Chalan Kareta

Status: Survey completed.
Design on hold by the DOD.
Estimated Const. Cost: \$60.7M
Designer: SSFM International

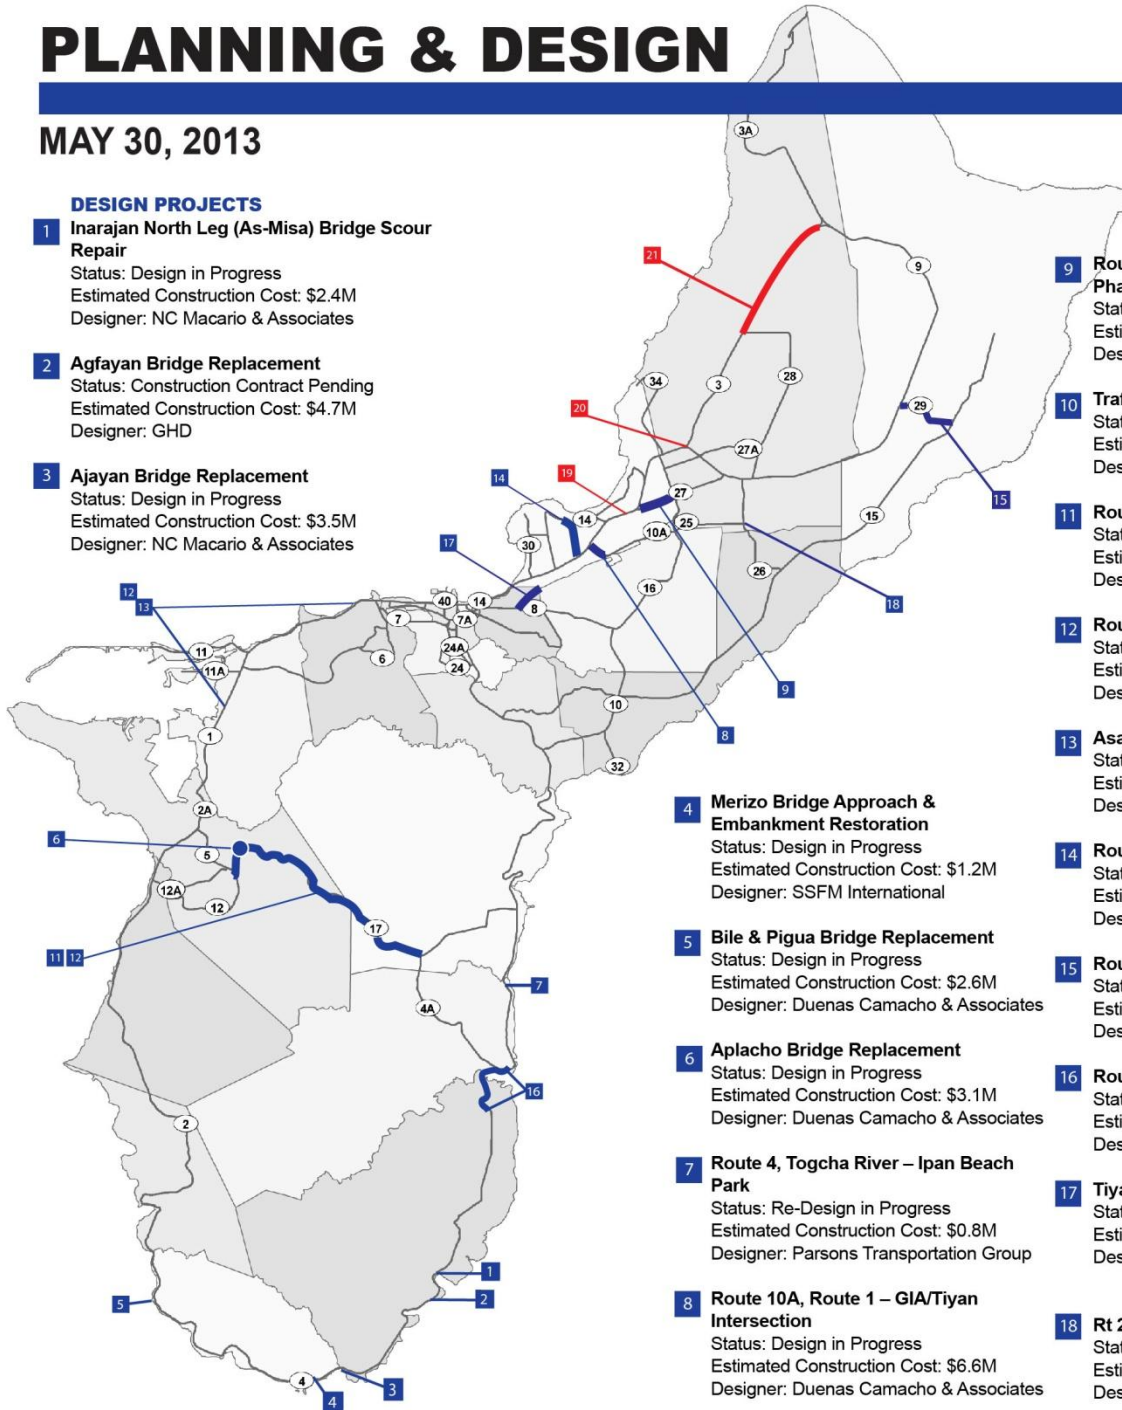

4 Merizo Bridge Approach & Embankment Restoration

Status: Design in Progress
Estimated Construction Cost: \$1.2M
Designer: SSFM International

5 Bile & Pigua Bridge Replacement

Status: Design in Progress
Estimated Construction Cost: \$2.6M
Designer: Duenas Camacho & Associates

6 Aplacho Bridge Replacement

Status: Design in Progress
Estimated Construction Cost: \$3.1M
Designer: Duenas Camacho & Associates

7 Route 4, Togcha River – Ipan Beach Park

Status: Re-Design in Progress
Estimated Construction Cost: \$0.8M
Designer: Parsons Transportation Group

8 Route 10A, Route 1 – GIA/Tiyan Intersection


Status: Design in Progress
Estimated Construction Cost: \$6.6M
Designer: Duenas Camacho & Associates

GARVEE Bond

Status of Authorized Projects

Project	Estimated Cost	Status
Tiyan Parkway, Phase 1	\$15.5 Million	Design 75% complete ROW MOU pending w/ GIAA, DLM IFB uncertain due to ROW
Rte 14B (Ypao Rd), Phase 1	\$ 5.4 Million	Design 95% complete Unanticipated ROW, 16 parcels IFB uncertain due to ROW
Rte 14B (Ypao Rd), Phase 2	\$ 5.9 Million	Design 80% complete ROW acquisition, 13 parcels IFB uncertain due to ROW
Rte 27 (Hamburger Rd), Phase 1	\$12.7 Million	Design 95% complete ROW condemnation likely IFB target 2014
TOTAL	\$39.5 Million	

Tiyan Parkway

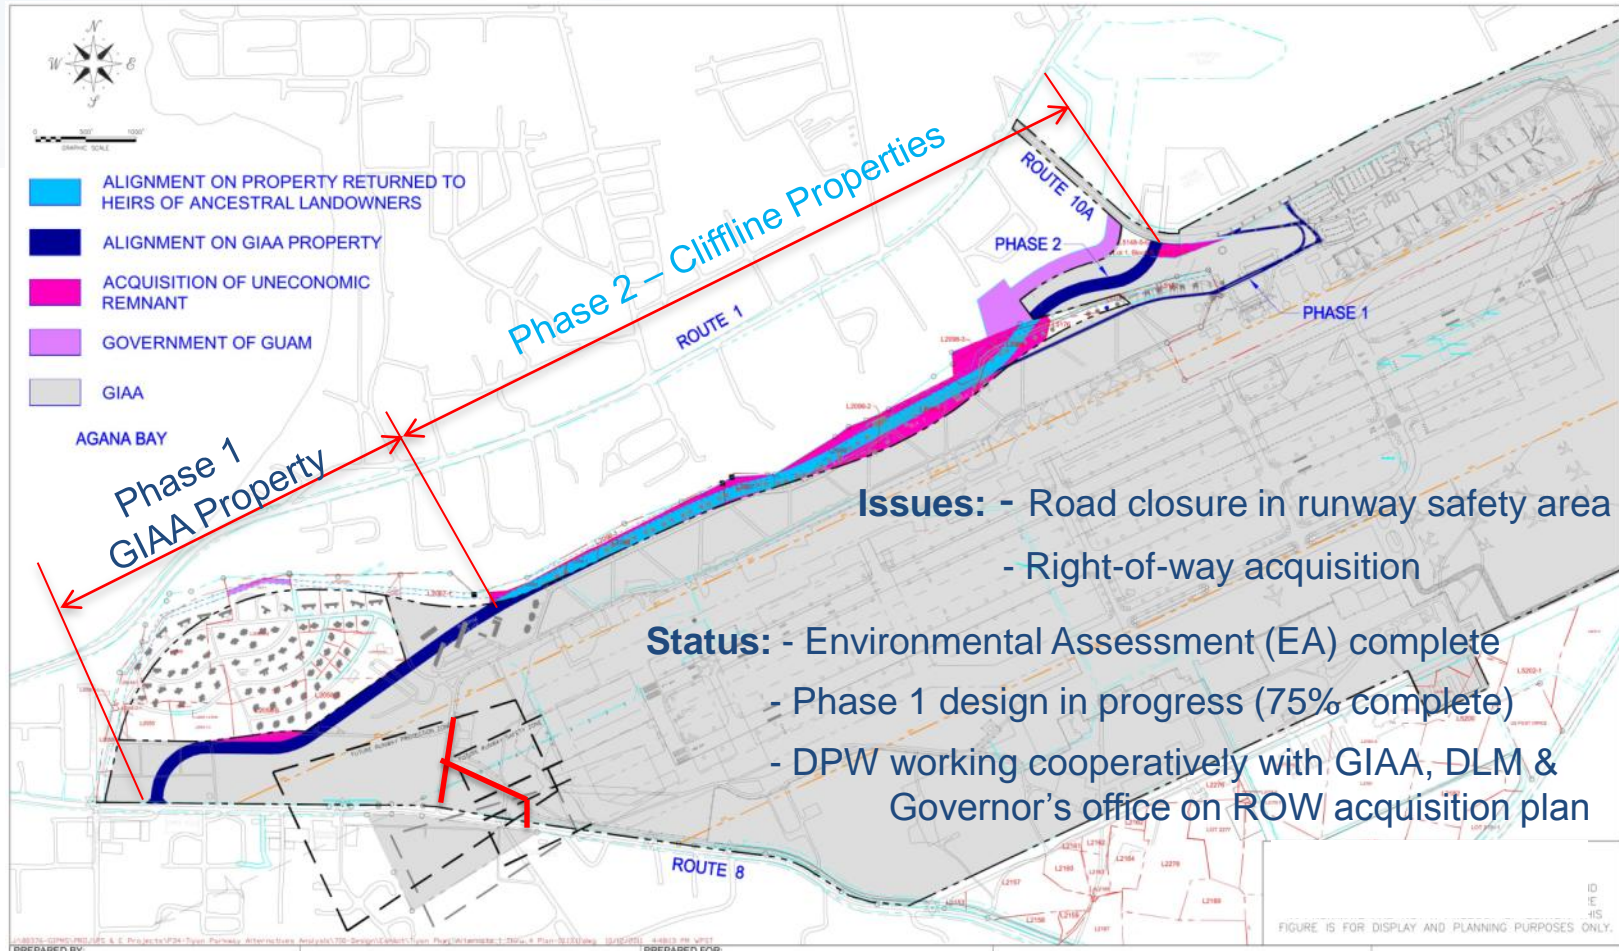

Alignment Alternate 4
